


EASTWOOD CARPARK

Construction Update June 2021

Upcoming Works

- Finalisation of Level 3 Western side slab formwork deck.
- Installation of steel reinforcement, post tension cables and cast in services to Level 3 Western side slab.
- Pouring of Level 3 Western side suspended concrete slab with curing methodology and stressing of post tension cabling.
- Installation of steel reinforcement, post tension cables and cast in services to Level 3 Eastern side slab.
- Pouring of Level 3 Eastern side suspended concrete slab.
- Permanent Power Connection

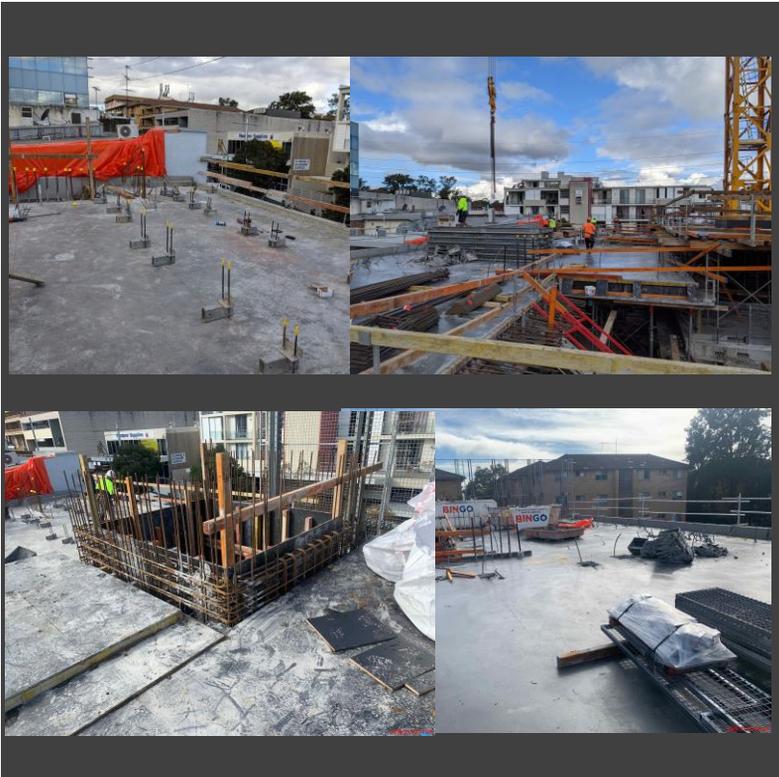

Completed Works

- ✓ Level 2 Western side suspended concrete slab Installation of steel reinforcement, post tension cables and cast in services to Level 2 Eastern side slab.
- ✓ Level 2 Eastern side suspended concrete slab poured and cured with initial stress of post tension cables complete.
- ✓ Level 2 precast concrete panels
- ✓ Installation of conduits for permanent power
