



Project: Project Plan Final Draft  
Date: Tue 15/02/11

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

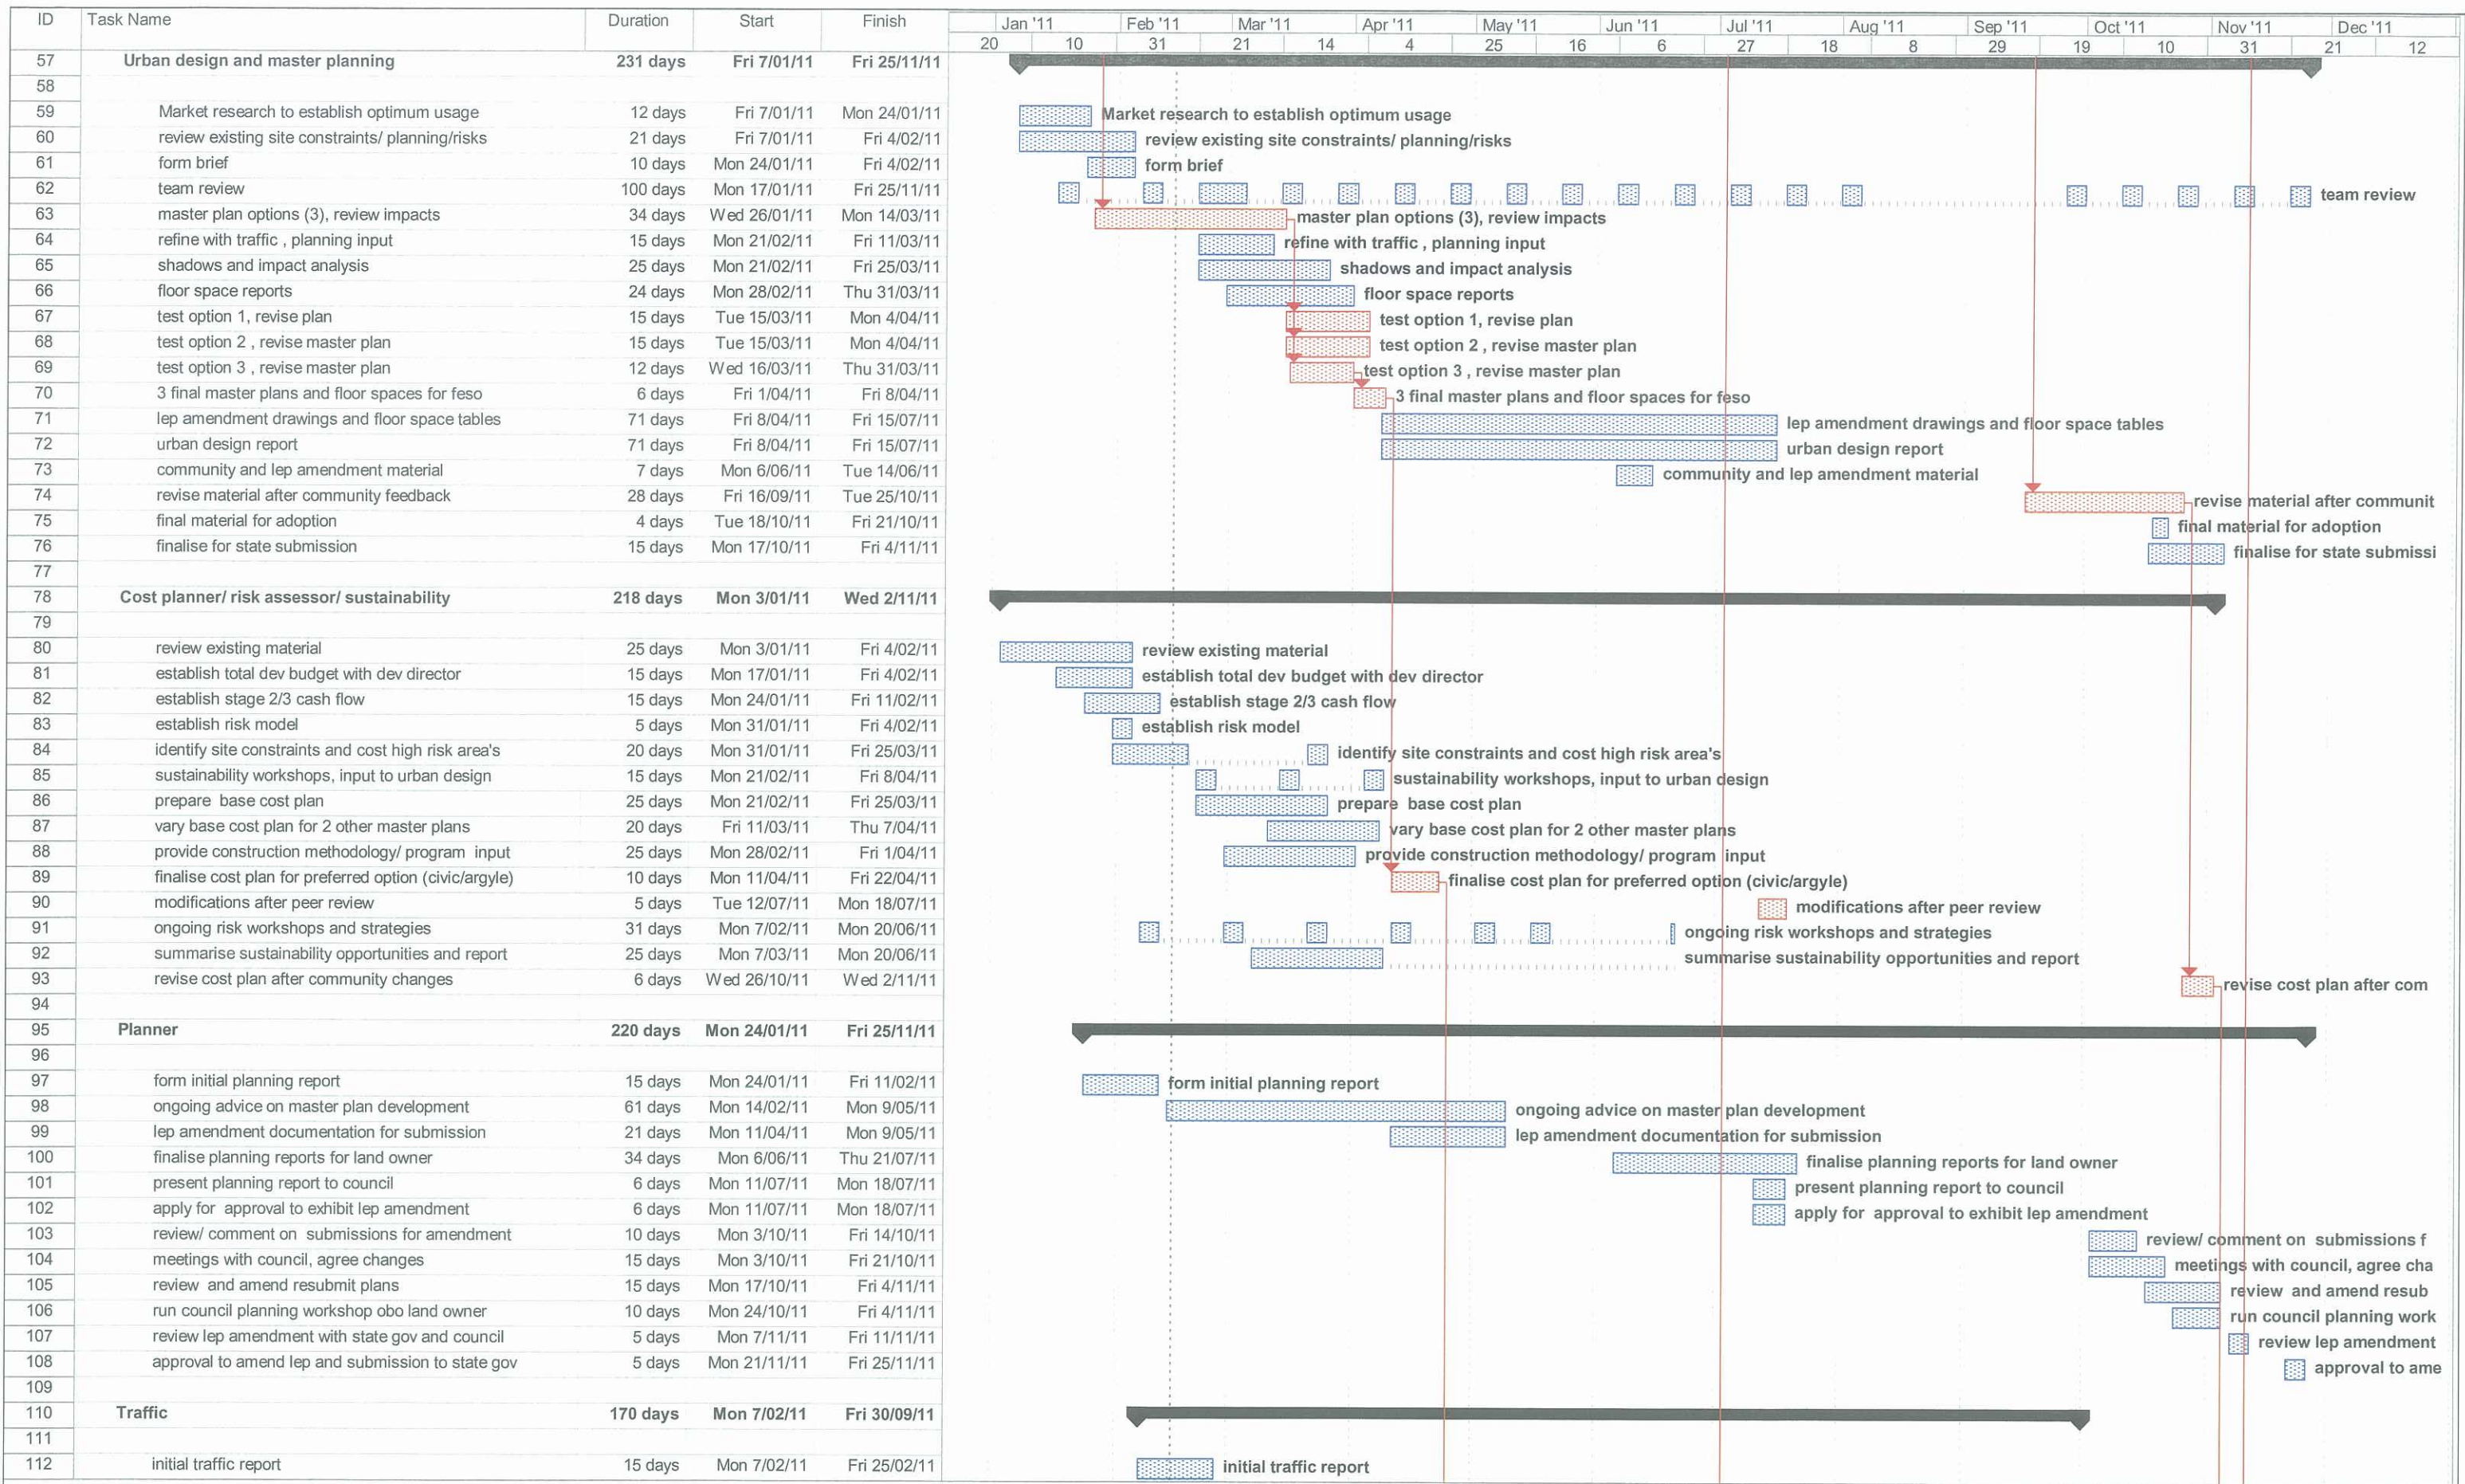

Project: Project Plan Final Draft  
Date: Tue 15/02/11

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

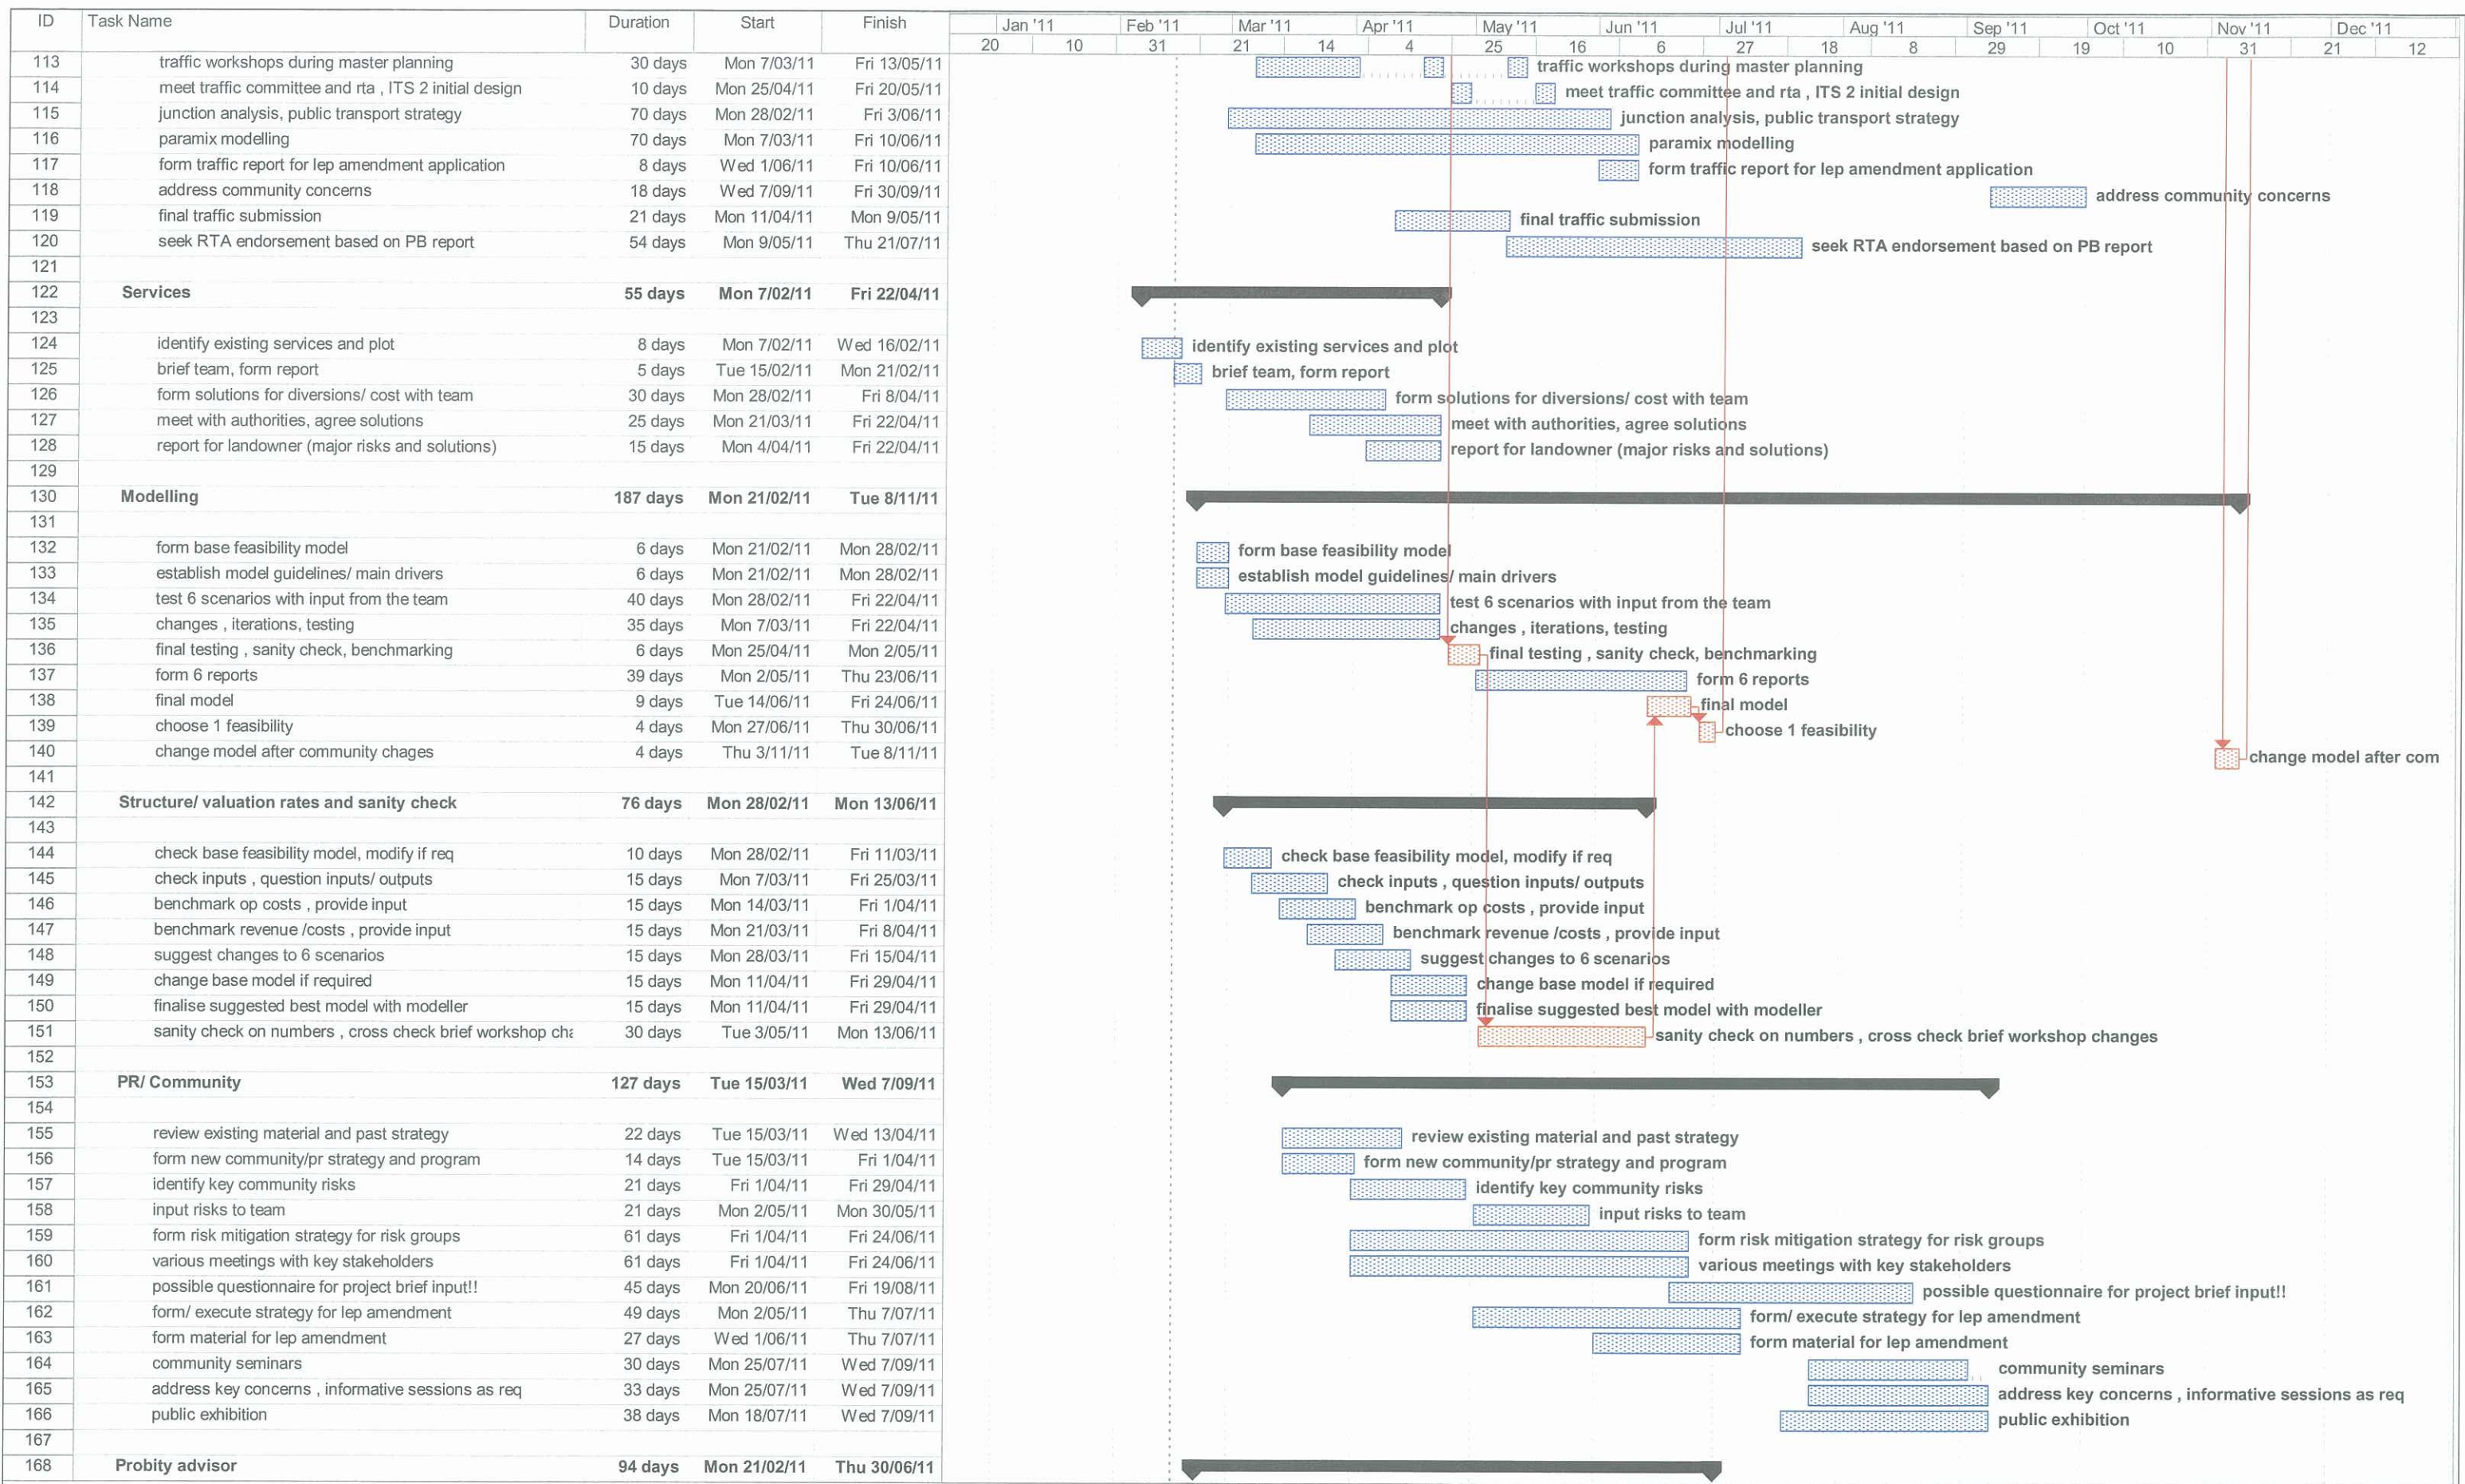


Project: Project Plan Final Draft  
Date: Tue 15/02/11

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

ID	Task Name	Duration	Start	Finish	Jan '11		Feb '11		Mar '11		Apr '11		May '11		Jun '11		Jul '11		Aug '11		Sep '11		Oct '11		Nov '11		Dec '11	
					20	10	31	21	14	4	25	16	6	27	18	8	29	19	10	31	21	12						
169																												
170	check procurement methods	5 days	Mon 21/02/11	Fri 25/02/11																								
171	review probity plan, suggest changes	10 days	Mon 28/02/11	Fri 11/03/11																								
172	advise team on changes in process due to probity	10 days	Mon 28/02/11	Fri 11/03/11																								
173	review lep amendment process, team, conflicts	10 days	Mon 28/02/11	Fri 11/03/11																								
174	advise planners on process changes	20 days	Mon 7/03/11	Fri 1/04/11																								
175	advise land owner of material req for public review	25 days	Mon 2/05/11	Fri 3/06/11																								
176	produce probity report for planning dept	30 days	Fri 20/05/11	Thu 30/06/11																								
177																												
178	<b>Stratum lawyer/ Surveyor</b>	<b>219 days</b>	<b>Mon 3/01/11</b>	<b>Thu 3/11/11</b>																								
179																												
180	review existing land holdings	15 days	Mon 21/02/11	Fri 11/03/11																								
181	import all title data, change base plans (CAD)	20 days	Mon 3/01/11	Fri 28/01/11																								
182	plot all service data	15 days	Mon 31/01/11	Fri 18/02/11																								
183	form project plan for amalgamation	25 days	Mon 21/03/11	Fri 22/04/11																								
184	review road closures and impact	44 days	Tue 1/02/11	Fri 1/04/11																								
185	road closure process	132 days	Tue 1/03/11	Wed 31/08/11																								
186	form amalgamation strategy , advise team	80 days	Mon 16/05/11	Fri 2/09/11																								
187	review easements	23 days	Thu 14/04/11	Mon 16/05/11																								
188	review proposed amalgamation with LPI	20 days	Mon 5/09/11	Fri 30/09/11																								
189	revise easements through amalgamation	15 days	Mon 3/10/11	Fri 21/10/11																								
190	report to council for amalgamation	14 days	Mon 17/10/11	Thu 3/11/11																								
191																												
192	<b>legal's , tax / structuring /finance</b>	<b>75 days</b>	<b>Mon 21/02/11</b>	<b>Fri 3/06/11</b>																								
193																												
194	review existing title structure	20 days	Mon 21/02/11	Fri 18/03/11																								
195	outline legal risks with proposed structure	46 days	Mon 28/02/11	Mon 2/05/11																								
196	restructure titles if required	68 days	Mon 28/02/11	Wed 1/06/11																								
197	review fund requirements	20 days	Mon 28/03/11	Fri 22/04/11																								
198	review project structure for roll out	35 days	Mon 11/04/11	Fri 27/05/11																								
199	review tax, GST, SD, land tax, change model	35 days	Mon 7/03/11	Fri 22/04/11																								
200	gain finance advice, lending criteria	25 days	Mon 14/03/11	Fri 15/04/11																								
201	form high level legal structure	45 days	Mon 28/03/11	Fri 27/05/11																								
202	test structure and governance meets brief	10 days	Mon 23/05/11	Fri 3/06/11																								

Project: Project Plan Final Draft  
Date: Tue 15/02/11

Task		Milestone		Rolled Up Critical Task		Split		Group By Summary	
Critical Task		Summary		Rolled Up Milestone		External Tasks		Deadline	
Progress		Rolled Up Task		Rolled Up Progress		Project Summary			

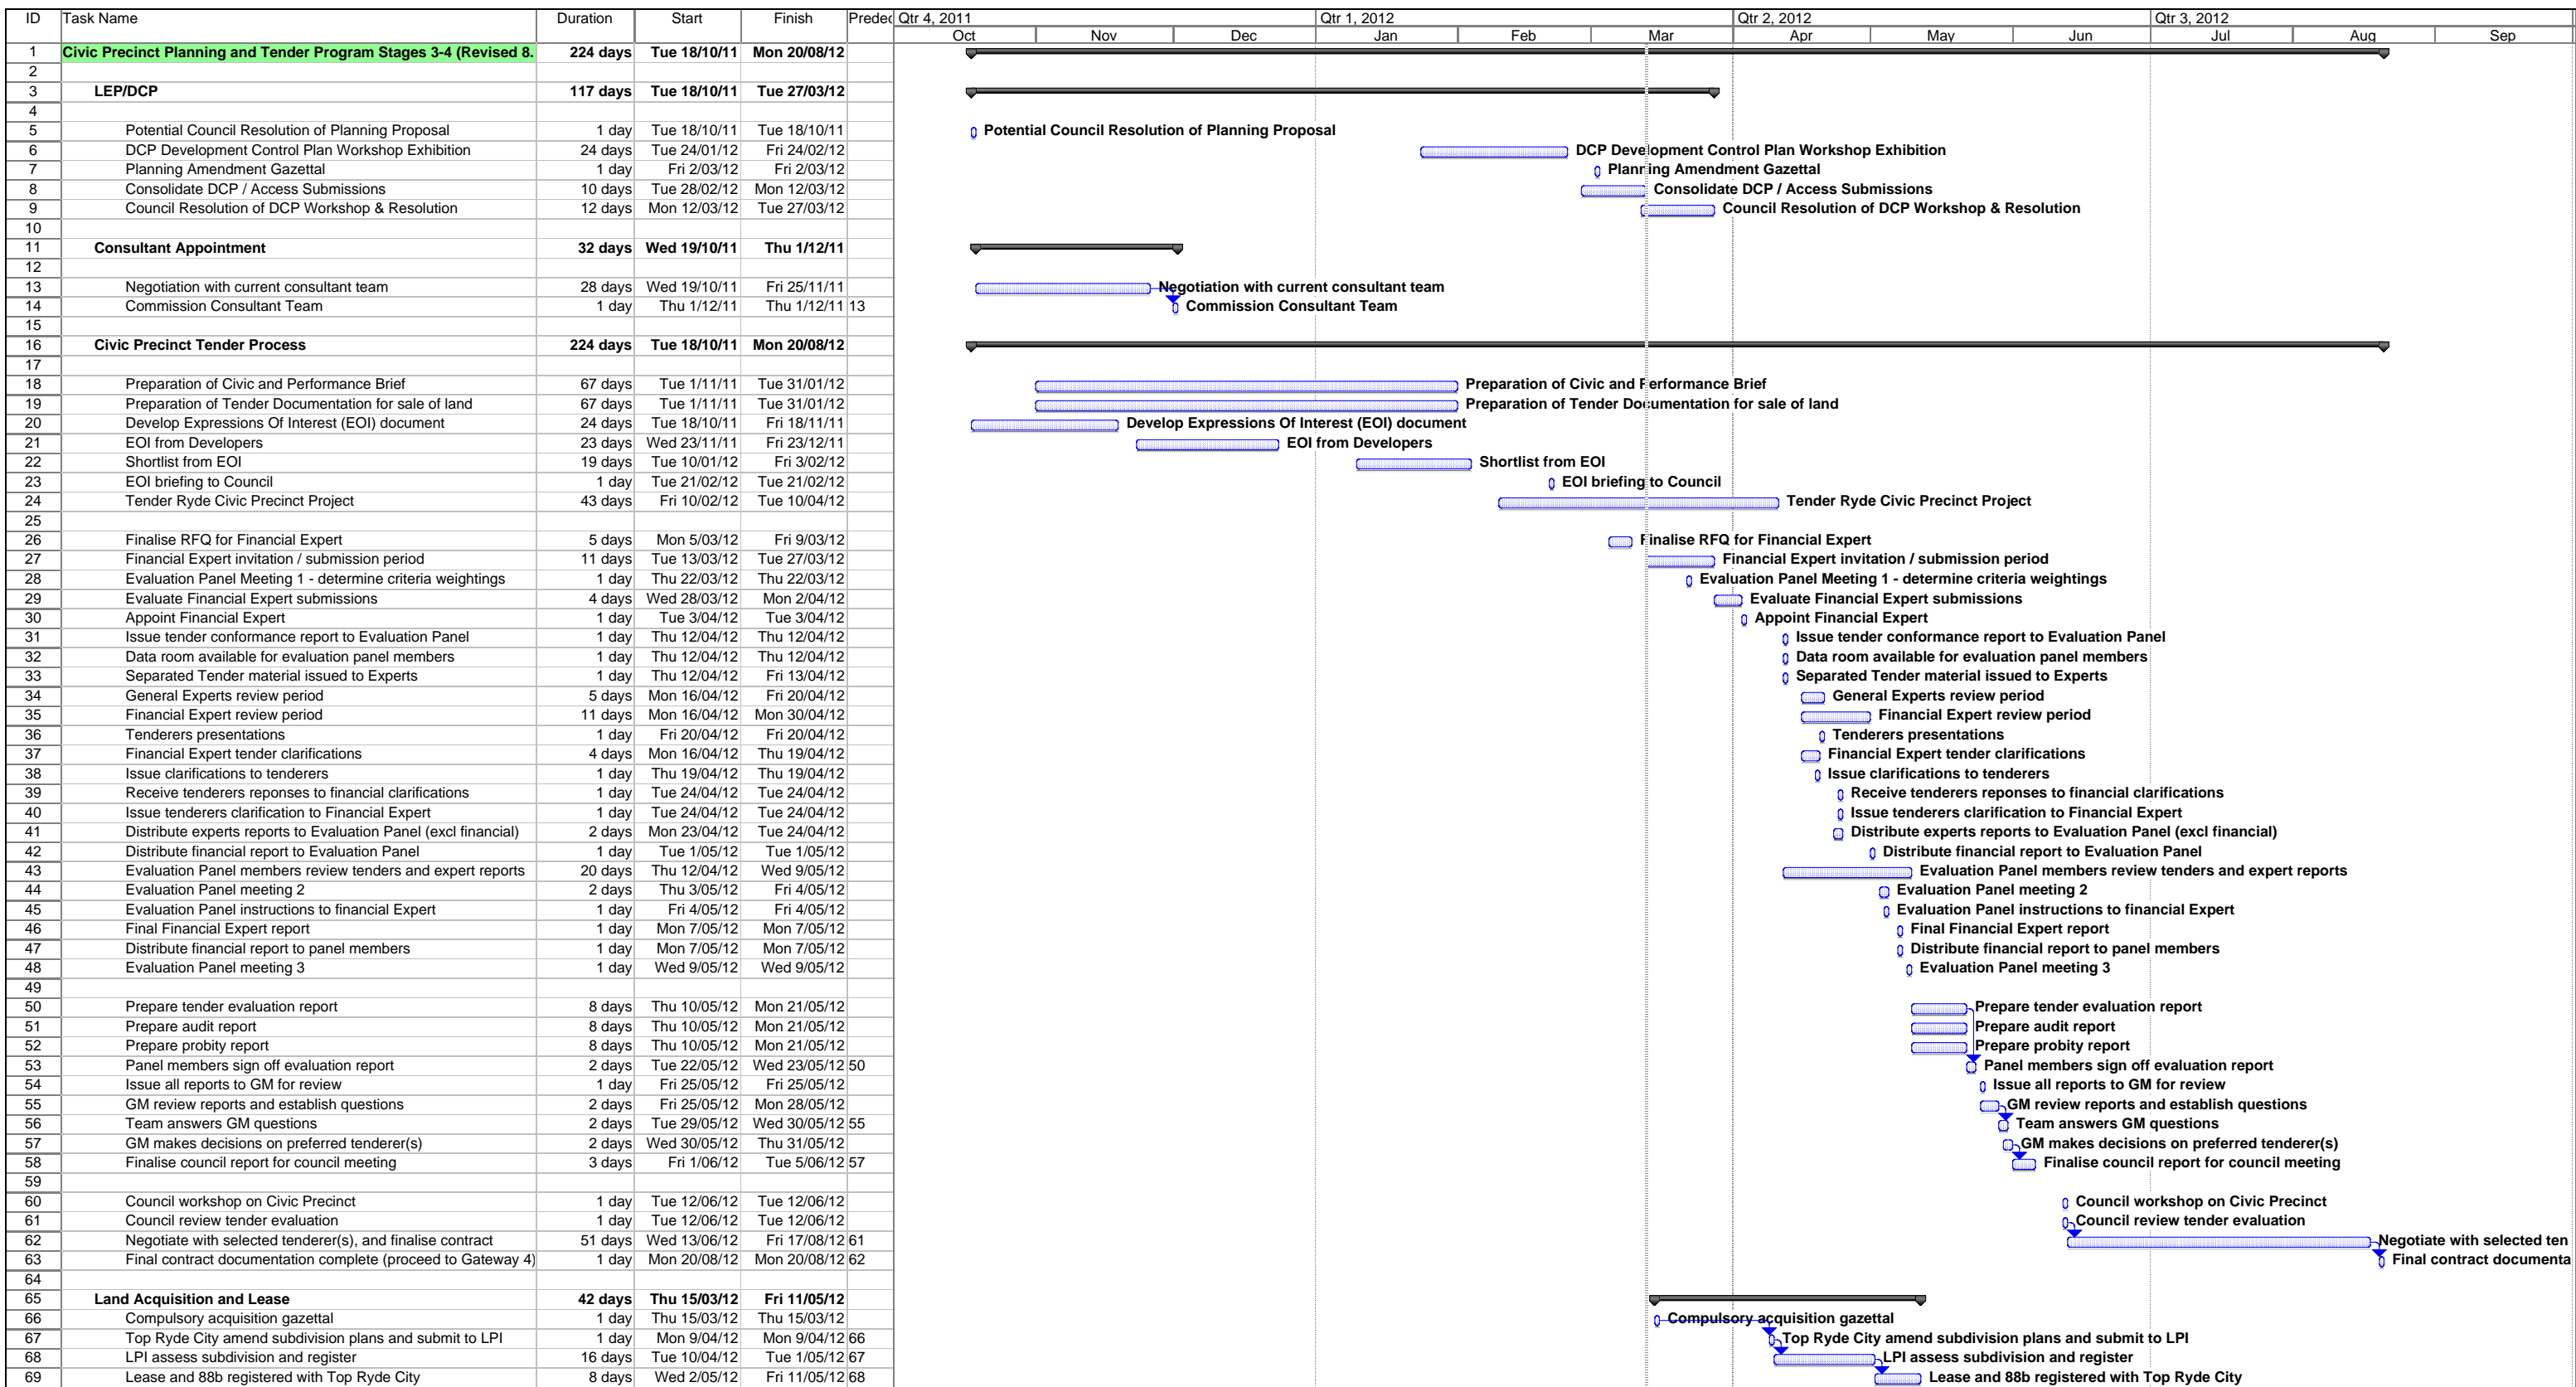

Project: Project Plan Final Draft  
Date: Tue 13/03/12

Task: [Blue bar] Progress, [Red bar] Milestone, [Grey bar] Summary, [Black bar] Rolled Up Critical Task, [White bar] Rolled Up Progress, [Dotted bar] External Tasks, [Light blue bar] Group By Summary

Critical Task: [Red bar] Milestone, [Black bar] Rolled Up Task, [Blue bar] Rolled Up Milestone, [White bar] Split, [Dotted bar] Project Summary, [Grey bar] Deadline
